

M/V "STAR SKY"

DRAUGHT SURVEY REPORT

PGUA/DS/287/25

CONTENTS	PAGE
1) PERSONS CONTACTED/ WITNESSES:	02
2) SHIP'S PARTICULARS	03
3) HOLD'S CAPACITIES / CARGOES / QUANTITIES / SF	03
4) SHIP'S HYDROSTATIC AND TANKS SOUNDING TABLES:	03
5) LOAD LINES	04
6) INITIAL DRAUGHT SURVEY DETAILS	04
7) FINAL DRAUGHT SURVEY DETAILS	04
8) CARGO PARTICULARS	04
9) DRAUGHT SURVEY CERTIFICATE	05
10) INITIAL BALLAST CONDITION	06
11) FINAL BALLAST CONDITION	06
12) INITIAL FRESH WATER CONDITION	07
13) FINAL FRESH WATER CONDITION	07
14) DEDUCTIBLES	07

ANNEXES

- SHIP'S PARTICULARS;
- CREW LIST;
- PRE-STOWAGE PLAN;
- LOADING SEQUENCE;
- DRAUGHT SURVEY CERTIFICATE
- FINAL CARGO PLAN;
- DETAILED CARGO PLAN PER LOADING TERMINAL;
- LINK TO THE DIGITAL DOCUMENTATION, PHOTOGRAPHS AND VIDEOS;



M/V "STAR SKY"
PGUA/DS/287/25
DRAUGHT SURVEY REPORT

THIS IS TO CERTIFY THAT the undersigned marine surveyor did, in compliance with instructions received from:

Messrs. Coamo Agroindustrial Cooperativa, Messrs. Cotriguaçu Cooperativa Central Regional Iguaçu Ltda., .

Attend on board the referenced vessel on September 20th, 2025 from 19:00 until 22:00 hours, whilst she was berthed alongside wharf 213, and on September 25th, 2025 from 16:10 until 18:00 hours, whilst she was berthed alongside wharf 213 at port of Paranaguá, Brazil, with views to perform the initial and final draft surveys, ascertaining the following figures:

1) PERSONS CONTACTED/ WITNESSES:

During the present survey, the following persons were contacted:

M/V "STAR SKY"

Mr. Archie Villamiel Alea, the Master
Mr. Ronaldo Angel Santos, the Chief Officer
Mr. Jaypee Aessor Labordo, the Chief Engineer

CARGILL AGRICOLA S/A
(As Local Agents)

Mr. Dirceu Rodrigo Pereira
Mr. Edmilson Adriano

PORTSOY OPERAÇÕES PORTUARIAS LTDA.
(As Port Operators)

Mr. Luiz Felipe Gori

STANDARD BRAZIL MARINE SURVEYS
& SERVICES LTDA.

Mr. José Antônio M. G. Pereira
the undersigned marine surveyor
Mr. Igor do Carmo C. Pinotti



2) SHIP'S PARTICULARS:

Vessel: STAR SKY
 Call sign: 5LRC8
 Port of Register: Monrovia
 Flag: Liberian
 IMO: 9399105
 LOA: 225,00
 LBP: 222,00
 Depth: 20,00
 Breadth: 32,26
 GRT: 42.604,0
 NRT: 26.602,0
 Classification: BV: Bulk Carrier BC-A (Holds 2,4 and 6 may be empty) ESP
 Unrestricted Navigation, AUT-UMS, MON-SHAFT, BWE,
 Inwatersurvey, EGCS-SCRUBBER, LI-HG-S1
 Light Ship: 11.768,0
 Summer deadweight/draft: 81466,00 on 14,40800 m
 Shipyard: Universal Shipbuilding Corporation, Maizuru Works.
 Owners: Star nor XI LLC.
 Operators: Star Bulk Management Inc.

3) HOLD'S CAPACITIES / CARGOES / QUANTITIES / SF

Hold	Capacity (cub.ft.)	Cargo	Quantity loaded (t) Exp. Corridor	SF
no.1	467.372,0	MIDDLE	8.718,425	53,61
no.2	495.168,0	SBMP	8.996,735	55,04
no.3	495.182,0	SBMP	9.280,180	53,36
no.4	472.895,0	SBMP	8.995,960	52,57
no.5	494.398,0	SBMP	9.596,990	51,52
no.6	495.701,0	SBMP	9.087,305	54,55
no.7	470.557,0	HIPRO	8.665,800	54,30
Total	3.391.273,0		63.341,395	

4)SHIP'S APPROVED HYDROSTATIC AND TANKS SOUNDING TABLES:

Hydrostatic table: Issued by Universal Shipbuilding Corporation.
 on 26.08.2010, Dwg. No. 1030150
 Approved by N/A on N/A

Sounding table: Issued by Universal Shipbuilding Corporation.
 on 21.06.2010 Dwg. no. 1033073



5) LOAD LINES

	FB (m)	Draught (m)	Displ. (t)	DWT (t)
Tropical Fresh Water:	5,011	15,042	95.272,0	83.504,0
Fresh Water:	5,311	14,742	93.231,0	81.463,0
Tropical:	5,345	14,708	95.325,0	83.557,0
Summer:	5,645	14,408	93.234,0	81.466,0
Winter:	5,945	14,108	91.143,0	79.375,0

6) INITIAL DRAUGHT SURVEY DETAILS:

Date: September 20th, 2025 from 19:00 until 22:00 hrs
 Place : Paranaguá, Brazil (wharf 213)
 Waves: 0,15 m
 Beaufort scale Wind force: 01
 Tide: Flood tide, >1knot
 Weather: Fine

7) FINAL DRAUGHT SURVEY DETAILS:

Date: September 25th, 2025 from 16:10 until 18:00 hrs
 Place : Paranaguá, Brazil (wharf 213)
 Waves: 0,30 m
 Beaufort scale Wind force: 02
 Tide: Flood tide, 1knot
 Weather: Rainy

8) CARGO PARTICULARS:

Cargo: Soybean meal in bulk
 Port of Loading: Port of Paranaguá, Brazil
 Port of Discharge: Amsterdam, Netherlands
 Last cargo: Coal in bulk
 Last Port: Sepetiba, Brazil

Shore Scales Figures: 63.341,395 t

Draught Survey Figures: STANDARD BRAZIL: 63.435,583 t
 MASTER/ CHIEF OFFICER: 63.440,210 t



M/V "STAR SKY"

IMO NO. 9399105 FLAG: Liberian BUILD: 2010

DRAUGHT SURVEY CERTIFICATE

PGUA/DS/287/25

	INITIAL SURVEY	FINAL SURVEY
	Wharf 213	Wharf 213
	20.09.2025 - 19:17 h	25.09.2025 - 16:20 h
	0,15 m. waves	0,30 m. waves
	Wind force 01	Wind force 02
	Flood tide, >1knot	Flood tide, 1knot
	Weather: Fine	Weather: Rainy
DRAUGHT	INITIAL	FINAL
Forward port	5,0800 m	12,0200 m
Forward starboard	4,9900 m	11,5800 m
Forward mean	5,0350 m	11,8000 m
Stem correction	-0,1030 m	-0,0392 m
Draught forward (corrected to fore perpendicular)	4,9320 m	11,7608 m
Midship port	5,6900 m	12,4300 m
Midship starboard	5,5800 m	11,8800 m
Midship mean	5,6350 m	12,1550 m
Midship correction	0,0000 m	0,0000 m
Draught midship (corrected to midship perpendicular)	5,6350 m	12,1550 m
Aft port	6,4300 m	12,5900 m
Aft starboard	6,4000 m	12,0600 m
Aft mean	6,4150 m	12,3250 m
Stern correction	0,1030 m	0,0392 m
Draught after (corrected to after perpendicular)	6,5180 m	12,3642 m
Kell correction	0,0000 m	0,0000 m
Means of means corrected:	5,6575 m	12,1319 m
True trim	BY STERN 1,59 m	BY STERN 0,60 m
Heel (angle & in cm)	P 0.20 ° 11,00 cm	P 0.98 ° 55,00 cm
Hull deflexion:	HOGGING 9,00 cm	SAGGING 9,25 cm
DISPLACEMENTS	INITIAL	FINAL
Displacement in salt water	34.262,7 t	77.395,0 t
First trim correction	-279,8 t	38,1 t
Second trim correction	11,0 t	1,4 t
Displacement corrected for trim	33.993,9 t	77.434,5 t
Water density	1,01900	1,01900
Displacement corrected for density	33.794,9 t	76.981,2 t
Deductibles (fresh water, oils, etc.)	21.546,4 t	1.297,2 t
Displacement corrected for deductibles	12.248,5 t	75.684,1 t
Light Ship	11.768,0 t	
Calculated constant	480,5 t	
Anchor + chain	0,0 t	0,0 t
Total cargo loaded on board as per draught survey		63435,6 t
Loading terminals: CO, CT, SH, .	TPC 63,8 t/cm	TPC 69,4 t/cm
Cargo: Soybean meal in bulk	MTC +0.5 915,1 t/cm	MTC +0.5 1166,6 t/cm
Paranaguá, Brazil. September 25th, 2025	MTC -0.5 895,7 t/cm	MTC -0.5 1149,9 t/cm
Total cargo loaded on board as per shore scales		63.341,395 t
Total cargo loaded on board as per draught survey		63.435,583 t
Surplus	94,188 t	0,15 %

Standard Brazil Marine Surveys & Services Ltda.
 José Antonio Machado Gomes Pereira / Igor do Carmo C. Pinotti
 Licensed Marine Officer / Marine Surveyor / 375460MM



Master/Ch.Off: 63.440,210 t 98,815 t 0,16 %

10) INITIAL BALLAST CONDITION:

Date / Time : 20.09.25 / 19:40 h Trim: 1,59 m

Vessel's	Observed	Pipe	Observed	Correction (m)		Corrected	Observed	Observed	Weight
Tank No.	Height (m)	A.D.L (m)	Sound. (m)	Trim	List	Sound. (m)	Volu. (m3)	Density	Total (t)
F.PK	24,55	0,33	9,94	-0,03	0,00	9,91	1502,21	1,020	1532,30
1 WBT (P)	20,98	0,33	19,98	-0,08	0,00	19,90	1285,20	1,02	1310,90
1 WBT (S)	20,98	0,33	20,14	-0,08	0,00	20,06	1306,22	1,02	1332,30
2 WBT (P)	21,00	0,33	19,78	-0,09	0,00	19,69	1474,50	1,02	1504,00
2 WBT (S)	21,00	0,33	19,86	-0,09	0,00	19,77	1491,58	1,02	1521,40
3 WBT (P)	21,00	0,33	19,50	-0,16	0,00	19,34	2713,96	1,02	2768,20
3 WBT (S)	21,00	0,33	19,80	-0,16	0,00	19,64	2851,66	1,02	2908,70
4 WBT (P)	20,82	0,32	20,39	-0,21	0,00	20,18	2433,18	1,02	2481,80
4 WBT (S)	20,82	0,32	20,63	-0,22	0,00	20,41	2476,14	1,02	2525,70
5 WBT (P)	22,10	0,73	22,03	0,00	0,00	22,03	1207,20	1,02	1231,30
5 WBT (S)	22,10	0,73	21,70	-0,03	0,00	21,67	1205,04	1,02	1229,10
A.PK	13,65	0,33	0,59	0,01	0,00	0,60	3,90	1,025	4,00
TOTAL							19950,79		20349,70

11) FINAL BALLAST CONDITION:

Date / Time : 25.09.25 / 16:55 h Trim: 0,60 m

Vessel's	Observed	Pipe	Observed	Correction (m)		Corrected	Observed	Observed	Weight
Tank No.	Height (m)	A.D.L (m)	Sound. (m)	Trim	List	Sound. (m)	Volu. (m3)	Density	Total (t)
F.PK	24,55	0,33	0,09	0,00	0,00	0,09	4,14	1,020	4,20
1 WBT (P)	20,98	0,33	0,03	0,00	0,00	0,03	13,94	1,02	14,20
1 WBT (S)	20,98	0,33	0,03	0,00	0,00	0,03	13,94	1,02	14,20
2 WBT (P)	21,00	0,33	0,03	0,00	0,00	0,03	16,26	1,02	16,60
2 WBT (S)	21,00	0,33	0,00	0,00	0,00	0,00	7,70	1,02	7,90
3 WBT (P)	21,00	0,33	0,01	0,00	0,00	0,01	14,50	1,02	14,80
3 WBT (S)	21,00	0,33	0,01	0,00	0,00	0,01	14,70	1,02	15,00
4 WBT (P)	20,82	0,32	0,03	0,00	0,00	0,03	13,10	1,02	13,40
4 WBT (S)	20,82	0,32	0,05	0,00	0,00	0,05	19,50	1,02	19,90
5 WBT (P)	22,10	0,73	0,70	0,00	0,00	0,70	6,71	1,02	6,80
5 WBT (S)	22,10	0,73	0,50	0,00	0,00	0,50	3,05	1,02	3,10
A.PK	13,65	0,33	0,59	0,00	0,00	0,59	3,82	1,025	3,90
TOTAL							131,36		134,00



12) INITIAL FRESH WATER CONDITION:

Vessel's	Observed	Pipe	Observed	Correction (m)		Corrected	Observed	Observed	Weight
Tank No.	Height (m)	A.D.L (m)	Sound. (m)	Trim	List	Sound. (m)	Volu. (m3)	Density	Total (t)
FWT (P)							70,00	1,000	70,00
DWT (S)							110,00	1,000	110,00
TOTAL							180,00		180,00

13) FINAL FRESH WATER CONDITION:

Vessel's	Observed	Pipe	Observed	Correction (m)		Corrected	Observed	Observed	Weight
Tank No.	Height (m)	A.D.L (m)	Sound. (m)	Trim	List	Sound. (m)	Volu. (m3)	Density	Total (t)
FWT (P)							70,00	1,000	70,00
DWT (S)							90,00	1,000	90,00
TOTAL							160,00		160,00

14) DEDUCTIBLES

	INITIAL	FINAL
INTERMEDIATE FUEL OIL	905,2 t	905,2 t
MARINE DIESEL OIL	111,5 t	98,0 t
LUBRICATING	K	K
FRESH WATER	180,0 t	160,0 t
BALLAST	20349,7 t	134,0 t
OTHERS	0,0 t	0,0 t
TOTAL	21546,4 t	1297,2 t



Digital documentation, photographs and videos:

MV STAR SKY

<https://standardbrazil.com.br/atendimentos/link?tag=PGUA/DS/287/25&tk=1616097708>



IMO CREW LIST

☒ Arrival

☐ Departure

Page No. 1

1. Name of the ship							2. Port of Arrival				3. Date of Arrival:	
M/V STAR SKY							PARANAGUA, BRAZIL				SEP 2025	
4. Nationality of ship							5. Last port of call:					
LIBERIA							SEPETIBA, BRAZIL					
No	Family name, given names	Rank	Sex	Nationality	Date of birth	Place of birth	Passport		Seaman's book		Place of embarkation	Date of embarkation
							Number	Exp. Date	Number	Exp. Date		
1	ALEA ARCHIE VILLAMIEL	Master	M	FILIPINO	3-Apr-1964	BATANGAS CITY	P6834840B	18 May 2031	C1098261	Jul 22,2027	XINGANG, CHINA	29-Apr-2025
2	SANTOS RONALDO ANGEL	C/Officer	M	FILIPINO	4-Apr-1970	ALEGRIA CEBU	P7583697A	18 Jun 2028	C1558292	Dec 03,2029	NANTONG, CHINA	19-May-2025
3	RETIRADO CARLO MAGNO ATIENZA	2/Officer	M	FILIPINO	21-Oct-1984	TOLEDO CITY	P5652560B	18 Oct 2030	C1229656	Apr 02,2028	NANTONG, CHINA	27-May-2025
4	SULADAY JENIL SACARE	3/Officer	M	FILIPINO	9-Jan-1986	BACOLOD CITY	P7401808A	31 May 2028	C1320734	Jul 13,2028	SINGAPORE	17-Apr-2025
5	LABORDO JAYPEE ASECOR	C/Engr.	M	FILIPINO	18-May-1985	LAMBUNAO ILOILO	P8143522B	09 Nov 2031	C1355311	May 10,2029	NANTONG, CHINA	19-May-2025
6	LOPEZ FLORENCIO JR. BALAO-AS	2/Engr.	M	FILIPINO	21-Aug-1986	BANGA S COTABATO	P6286213A	04 Mar 2028	C1226683	Mar 06,2028	NANTONG, CHINA	19-May-2025
7	CIPRIANO SYVEL GERARD LANDAUZ	3/Engr.	M	FILIPINO	27-Dec-1993	LEZO AKLAN	P6481886B	11 Mar 2031	C0987833	Apr 01,2027	SINGAPORE	17-Apr-2025
8	CADIZ BRIAN EDWARD BELOY	4/Engr.	M	FILIPINO	3-Dec-1990	MANILA	P6261130A	01 Mar 2028	C1418974	Nov 24,2028	XINGANG, CHINA	29-Apr-2025
9	DE VERA HUBERT PEDRO	ELECTR.	M	FILIPINO	5-Nov-1977	PASAY RIZAL	P5974883B	17 Dec 2030	C1462902	Mar 12,2029	NANTONG, CHINA	27-May-2025
10	LICERALDE BORROMEO JR. ESPINOSA	BOSUN	M	FILIPINO	24-Jun-1973	DASOL PGN	P4037330B	03 Dec 2029	C1042297	May 15,2027	HAMBURG, GERMANY	29-Nov-2024
11	DELOS REYES RONALD MERQUITA	AB1	M	FILIPINO	22-Nov-1992	BATANGAS CITY	P7604228B	14 Sep 2031	C0928265	Jan 25,2027	XINGANG, CHINA	29-Apr-2025
12	MADRIJANON JOREY ORDINARIO	AB2	M	FILIPINO	8-Oct-1989	KORONADAL SO COT	P1224872B	26 Mar 2029	C1392509	Apr 20,2029	XINGANG, CHINA	29-Apr-2025
13	MAGABILIN VINCENT NACIONALES	AB3	M	FILIPINO	5-Sep-1973	BARBAZA ANTIQUE	P0505423C	13 Jun 2032	C1159215	Sep 27,2027	NANTONG, CHINA	27-May-2025
14	RABAGO FRANZ KYLE BACULI	OS1	M	FILIPINO	3-Oct-1998	CEBU CITY	P7847449B	12 Oct 2031	C1309570	Aug 05,2028	NANTONG, CHINA	27-May-2025
15	LAÑA JYLMER ALESNA	OS2	M	FILIPINO	18-Feb-1994	CARCAR CEBU	P1625879B	10 May 2029	C1165942	Oct 12,2027	XINGANG, CHINA	29-Apr-2025
16	ARCEO MANUEL CLARO EBOL	D/Cdt	M	FILIPINO	11-Feb-2001	IROSIN SORSOGON	P4272323C	30 May 2033	A0244405	11 09 2033	NANTONG, CHINA	27-May-2025
17	GAVARRA RENATO GACIS	Oiler	M	FILIPINO	4-Sep-1972	MATNOG SORSOGON	P8062207B	02 Nov 2031	C1063785	Jun 17,2027	NANTONG, CHINA	27-May-2025
18	TANISTA IAN JEREL JED ALEGRO	Wiper	M	FILIPINO	27-May-1993	BACOLOD CITY	P3339144C	20 Feb 2033	C0926425	Jan 24,2027	XINGANG, CHINA	29-Apr-2025
19	CAFINO JOHN REY BERNALDO	E/Cdt	M	FILIPINO	17-Dec-1998	VALENZUELA MM	P8126664A	27 Jul 2028	C1261724	May 30,2028	NANTONG, CHINA	27-May-2025
20	SOLA JAYSON CAÑETE	Welder	M	FILIPINO	14-Nov-1987	SAN PASCUAL BVS	P5993365B	20 Dec 2030	A0289610	14 12 2033	BALBOA, PANAMA	19-Jul-2025
21	BILASA ARTHUR MANZANILLO	C/Cook	M	FILIPINO	10-Aug-1982	MANILA	P1099806B	18 Mar 2029	C1491430	Jun 10,2029	SINGAPORE	17-Apr-2025
22	BOHOL ENRYK ANTHONY	Messman	M	FILIPINO	16-Sep-2000	KALIBO AKLAN	P8125992C	03 Oct 2034	A0141834	18 10 2033	NANTONG, CHINA	27-May-2025




STARBULK MNGT INC.**M.V. STAR SKY**
Monrovia**PRE-STOWAGE PLAN**

DATE	10-Sep-25
VOYAGE NO.	37
LOADING PORT	Paranagua, Brazil
DISCH PORT	Amsterdam, Netherlands
CARGO	SBM
QUANTITY	61,651.00mt

SBM	Amaggi	Cefetra		%	%
HOLD 1		8,496.0mt			100 %
HOLD 2	9,003.0mt			100 %	
HOLD 3		9,002.0mt			100 %
HOLD 4	8,598.0mt			100 %	
HOLD 5		8,986.0mt			100 %
HOLD 6	9,012.0mt			100 %	
HOLD 7		8,554.0mt			100 %
TOTAL	26,613.0mt	35,038.0mt			

Amaggi 26613.0mt**Cefetra 35038.0mt****TOTAL = 61651.0mt**

	Dep. Paranagua	Arr. Amsterdam
FWD	11.55 m	11.53 m
MEAN	11.95 m	11.84 m
AFT	12.35 m	12.14 m
TRIM	0.80 m	0.61 m
Density	1.016	1.025

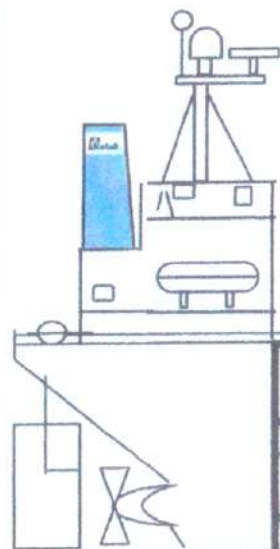

8,554mt SBM	9,012mt SBM	8,986mt SBM	8,598mt SBM	9,002mt SBM	9,003mt SBM	8,496mt SBM
SF 55 CUFT/MT	SF 54.99 CUFT/MT	SF 54.99 CUFT/MT	SF 54.99 CUFT/MT	SF 55 CUFT/MT	SF 54.99 CUFT/MT	SF 55 CUFT/MT
100 %	100 %	100 %	100 %	100 %	100 %	100 %
Braz hipro/Cefetra	Amaggi	Pellets / Cefetra	Amaggi	Pellets / Cefetra	Amaggi	Mid. hipro/Cefetra
HOLD NO.7	HOLD NO.6	HOLD NO.5	HOLD NO.4	HOLD NO.3	HOLD NO.2	HOLD NO.1
Amsterdam	Amsterdam	Amsterdam	Amsterdam	Amsterdam	Amsterdam	Amsterdam

61,651.00mt**C/O: Ronaldo A. Santos**
Chief Officer**Capt. Archie V. Alea**
Master**Remarks: Cargo Figures are subject to following parameters and conditions:**

- 1) ABOVE QUANTITY IS THE MAXIMUM THEORETICAL CARGO INTAKE AS PER CHARTERERS' REQUEST AND ALL QUANTITIES ARE ON ABOUT BASIS.
- 2) FINAL CARGO QUANTITY IS SUBJECT TO THE ACTUAL WEIGHTS AT THE END OF THE LOADING, ACTUAL STOWAGE FACTOR OF THE CARGO(S), VESSEL'S STABILITY INCLUDING GRAIN INTACT STABILITY IN CASE OF GRAIN LOADING, TRIM, STRESSES, DEFLECTION (HOGGING OR SAGGING), PROPER TRIMMING AND DISTRIBUTION OF CARGO BY STEVEDORES AS PER AGREED PLAN
- 3) DRAFT RESTRICTIONS AT ANY PORT OF CALL, ACTUAL SALINITY OF WATER ON COMPLETION OF LOADING, BUNKERING ETC.

M/V "STAR SKY"	INITIAL SURVEY		FINAL SURVEY	
	Wharf 213		Wharf 213	
	20.09.2025 - 19:17 h		25.09.2025 - 16:20 h	
	0,15 m. waves		0,30 m. waves	
IMO NO. 9399105 FLAG: Liberian BUILD: 2010	Wind force 01		Wind force 02	
DRAUGHT SURVEY CERTIFICATE	Flood tide, >1knot		Flood tide, 1knot	
PGUA/DS/287/25	Weather: Fine		Weather: Rainy	
DRAUGHT	INITIAL		FINAL	
Forward port	5,0800 m		12,0200 m	
Forward starboard	4,9900 m		11,5800 m	
Forward mean	5,0350 m		11,8000 m	
Stern correction	-0,1030 m		-0,0392 m	
Draught forward (corrected to fore perpendicular)	4,9320 m		11,7608 m	
Midship port	5,6900 m		12,4300 m	
Midship starboard	5,5800 m		11,8800 m	
Midship mean	5,6350 m		12,1550 m	
Midship correction	0,0000 m		0,0000 m	
Draught midship (corrected to midship perpendicular)	5,6350 m		12,1550 m	
Aft port	6,4300 m		12,5900 m	
Aft starboard	6,4000 m		12,0600 m	
Aft mean	6,4150 m		12,3250 m	
Stern correction	0,1030 m		0,0392 m	
Draught after (corrected to after perpendicular)	6,5180 m		12,3642 m	
Kell correction	0,0000 m		0,0000 m	
Means of means corrected:	5,6575 m		12,1319 m	
True trim	BY STERN	1,59 m	BY STERN	0,60 m
Heel (angle & in cm)	P 000 °	11,00 cm	P 001 °	55,00 cm
Hull deflexion:	HOGGING	9,00 cm	SAGGING	9,25 cm
DISPLACEMENTS	INITIAL		FINAL	
Displacement in salt water	34.262,7 t		77.395,0 t	
First trim correction	-279,8 t		38,1 t	
Second trim correction	11,0 t		1,4 t	
Displacement corrected for trim	33.993,9 t		77.434,5 t	
Water density	1,01900		1,01900	
Displacement corrected for density	33.794,9 t		76.981,2 t	
Deductibles (fresh water, oils, etc.)	21.546,4 t		1.297,2 t	
Displacement corrected for deductibles	12.248,5 t		75.684,1 t	
Light Ship	11.768,0 t			
Calculated constant	480,5 t			
Anchor + chain	0,0 t		0,0 t	
Total cargo loaded on board as per draught survey			63435,6 t	
Loading terminals: CO, CT, SH, .	TPC	63,8 t/cm	TPC	69,4 t/cm
Cargo: Soybean meal in bulk	MTC +0.5	915,1 t*cm	MTC +0.5	1166,6 t*cm
Paranaguá, Br - Brazil. September 25th, 2025	MTC -0.5	895,7 t*cm	MTC -0.5	1149,9 t*cm
Total cargo loaded on board as per shore scales			63.341,395 t	
Total cargo loaded on board as per draught survey			63.435,583 t	
Surplus	94,188 t		0,15 %	

Standard Brazil Marine Surveys & Services Ltda.
 José Antonio Machado Gomes Pereira / Igor do Carmo C. Pinotti
 Licensed Marine Officer / Marine Surveyor / 375460MM

Master/Ch.Off: 63.440,210 t 98,815 t 0,16 %



www.standardbrazil.com.br

PortSoy



STOWAGE PLAN

MV STAR SKY

Loading Port : PARANAGUA, BRAZIL

Date . . : September 25th, 2025

Discharging Port . . : EUROPEAN PORT(S)

Cargo : 63.341,395 BRAZ. EXTRACTED TOASTED SOYBEANMEAL/PELLETS/MIDDLE HIPRO/HIPRO

Average Stowage Factor : 53,56

	Hold 7	Hold 6	Hold 5	Hold 4	Hold 3	Hold 2	Hold 1	STAR SKY
	FULL	FULL	FULL	FULL	FULL	FULL	FULL	
	8.665,800	9.087,305	9.596,990	8.995,960	9.280,180	8.996,735	8.718,425	
	M/Tons	M/Tons	M/Tons	M/Tons	M/Tons	M/Tons	M/Tons	
	HIPRO	SMB	SMB	SMB	SMB	SMB	MIDDLE HP	
Cubic Capacity	470,557	495,701	494,398	472,895	495,182	495,168	467,372	
Stowage Factor	54,30	54,55	51,52	52,57	53,36	55,04	53,61	



Master or Chief Officer
MV STAR SKY

Portsoy Port Operators



REMARK: Weight, measure, quality, quantity, condition, contents and value unknown.

NAVIO:	STAR SKY
AGÊNCIA:	CARGILL AGRICOLA S/A
OPERADOR:	PORTSOY OPERAÇÕES PORTUARIAS LTDA.
DATA EMBARQUE:	25.09.2025
PESO TERRA:	63.341,395
PESO BORDO:	63.435,583
VARIAÇÃO:	94,188
PERCENTUAL:	0,15%
Entrar na estatística	Sim

PORÃO	1	2	3	4	5	6	7	TOTAL
PRODUTO	MIDDLE	SBMP	SBMP	SBMP	SBMP	SBMP	HIPRO	
AGTL								0,000
CARGILL								0,000
CENTRO SUL								0,000
CIMBESSUL								0,000
COAMO	8.718,425		9.280,180		9.596,990		8.665,800	36.261,395
CORREDOR - V								0,000
CORREDOR - H		8.500,000						8.500,000
COTRIGUAÇU		496,735		8.995,960		9.087,305		18.580,000
INTERALLI								0,000
DREYFUS								0,000
ROCHA								0,000
TOTAL	8.718,425	8.996,735	9.280,180	8.995,960	9.596,990	9.087,305	8.665,800	63.341,395
CUBAGEM	467.372	495.168	495.182	472.895	494.398	495.701	470.557	
FATOR DE ESTIVA	53,61	55,04	53,36	52,57	51,52	54,55	54,30	
CONDIÇÃO PORÃO	FULL	FULL	FULL	FULL	FULL	FULL	FULL	

Observações:
