

MV "LAAX"

DRAUGHT SURVEY REPORT

PGUA/DS/304/25

CONTENTS

PAGE

1) PERSONS CONTACTED/ WITNESSES:	02
2) SHIP'S PARTICULARS	03
3) HOLD'S CAPACITIES / CARGOES / QUANTITIES / SF	03
4) SHIP'S HYDROSTATIC AND TANKS SOUNDING TABLES:	03
5) LOAD LINES	04
6) INITIAL DRAUGHT SURVEY DETAILS	04
7) FINAL DRAUGHT SURVEY DETAILS	04
8) CARGO PARTICULARS	04
9) DRAUGHT SURVEY CERTIFICATE	05
10) INITIAL BALLAST CONDITION	06
11) FINAL BALLAST CONDITION	06
12) INITIAL FRESH WATER CONDITION	07
13) FINAL FRESH WATER CONDITION	07
14) CONSUMABLES / OILS	07

ANNEXES

- SHIP'S PARTICULARS;
- CREW LIST;
- PRE-STOWAGE PLAN;
- LOADING SEQUENCE;
- DRAUGHT SURVEY CERTIFICATE
- FINAL CARGO PLAN;
- DETAILED CARGO PLAN PER LOADING TERMINAL;
- LINK TO THE DIGITAL DOCUMENTATION, PHOTOGRAPHS AND VIDEOS;



MV "LAAX"
PGUA/DS/304/25
DRAUGHT SURVEY REPORT

THIS IS TO CERTIFY THAT the undersigned marine surveyor did, in compliance with instructions received from:

Messrs. Cimbessul Terminal Portuario S/A, Messrs. Coamo Agroindustrial Cooperativa, Messrs. Cotriguaçu Cooperativa Central Regional Iguaçu Ltda., Messrs. Rocha Terminais Portuários e Logística .

#NOME?

1) PERSONS CONTACTED/ WITNESSES:

During the present survey, the following persons were contacted:

MV "LAAX"

Mr. Oleksandr Tykholaz, the Master
Mr. Denis Shcherbaney, the Chief Officer
Mr. Sergiy Kraslyuk, the Chief Engineer

AGÊNCIA MARITIMA CARGONAVE LTDA
(As Local Agents)

Mr. Renan Calixto
Mr. Rafael Nogueira
Mr. Lorram Gabriel Florentino

AGÊNCIA MARITIMA CARGONAVE LTDA
(As Port Operators)

Mr. Azemir do Rosario
Mr. Willian Cordeiro

UNISURVEY LTDA.
(As Charterers surveyors)

Mr. Joni Nunes Carvalho
Mr. Ernesto Lara

SGS DO BRASIL S/A
(As Consignees surveyors)

Mr. Marcos Heringer

PH SERVICES LTDA
(As Cargo Receivers surveyors)

Mr. Paulo Henrique Souza

BRAZILIAN CUSTOMS SURVEYOR

Mr. Angela Ramos Guimarães Souza

STANDARD BRAZIL MARINE SURVEYS
& SERVICES LTDA.

Mr. José Antônio M. G. Pereira
the undersigned marine surveyor
Mr. Thiago Henrique Barbosa Verhagen



2) SHIP'S PARTICULARS:

Vessel: LAAX
 Call sign: V7XG9
 Port of Register: Majuro
 Flag: Marshall Islands
 IMO: 9512355
 LOA: 228,99
 LBP: 222,00
 Depth: 20,05
 Breadth: 32,26
 GRT: 43.013,0
 NRT: 27.239,0
 Classification: NKK NS*(CSR, BC-A, BC-XII, GRAB 20, PSPC-WBT),
 (IWS)(IHM), MNS*, Strengthened for heavy cargoes loading,
 Holds no. 2,4 & 6 may be empty.
 Light Ship: 12.085,0
 Summer deadweight/draft: 82,265.0 on 14.43 m
 Shipyard: Tsuneishi Shipbuilding Co., Ltd.
 Owners: Bailey Navigation Company - Marshall islands
 Operators: Grehel Shipmanagement Co. - Greece

3) HOLD'S CAPACITIES / CARGOES / QUANTITIES / SF

Hold	Capacity (cub.ft.)	Cargo	Quantity loaded (t) Exp. Corridor	SF
no.1	445.764,0	MAIZE	9.440,940	47,22
no.2	520.176,0	MAIZE	10.848,900	SLACK
no.3	508.059,0	MAIZE	11.054,775	45,96
no.4	448.443,0	MAIZE	9.749,040	46,00
no.5	506.869,0	MAIZE	11.084,795	45,73
no.6	503.740,0	MAIZE	7.903,120	SLACK
no.7	505.993,0	MAIZE	10.805,640	46,83
Total	3.439.044,0		70.887,210	

4)SHIP'S APPROVED HYDROSTATIC AND TANKS SOUNDING TABLES:

Hydrostatic table: Issued by Tsuneishi Shipbuilding Co., Ltd.
 on 14.12.2011, Dwg. No. 150800

Sounding table: Issued by Tsuneishi Shipbuilding Co., Ltd.
 on 18.11.2011 Dwg. no. 150610W



5) LOAD LINES

	FB (m)	Draught (m)	Displ. (t)	DWT (t)
Tropical Fresh Water:	5,043	15,062	96.409,0	84.324,0
Fresh Water:	5,343	14,762	94.342,0	82.257,0
Tropical:	5,376	14,729	96.468,0	84.383,0
Summer:	5,676	14,429	94.350,0	82.265,0
Winter:	5,976	14,129	92.233,0	80.148,0

6) INITIAL DRAUGHT SURVEY DETAILS:

Date:	October 15th, 2025 from 7:40 until 0:00 hrs
Place :	Paranaguá, Br - Brazil (inner roads 9.1)
Waves:	0,10 m
Beaufort scale Wind force:	01
Tide:	No tide flow
Weather:	Fine

7) FINAL DRAUGHT SURVEY DETAILS:

Date:	October 18th, 2025 from 4:40 until 6:50 hrs
Place :	Paranaguá, Br - Brazil (wharf 213)
Waves:	0,10 m
Beaufort scale Wind force:	01
Tide:	No tide flow
Weather:	Cloudy

8) CARGO PARTICULARS:

Cargo:	Maize in bulk
Port of Loading:	Port of Paranaguá, Br - Brazil
Port of Discharge:	B.I.K - IRAN
Last cargo:	Coal in bulk
Last Port:	Fujairah - UAE

Shore Scales Figures: 70.887,210 t

Draught Survey Figures:

STANDARD BRAZIL:	70.975,777	t
MASTER/ CHIEF OFFICER:	70.968,800	t
CUSTOMS SURVEYOR :	70.969,692	t
OWNERS:	70.952,697	
CONSIGNEES SURVEYOR:	70.959,568	
RECEIVERS SURVEYOR:	70.962,921	



MV "LAAX"	INITIAL SURVEY		FINAL SURVEY	
	Inner roads 9.1		Wharf 213	
IMO NO. 9512355 FLAG: Marshall Island BUILD: 2012	15.10.2025 - 08:10 h		18.10.2025 - 04:50 h	
DRAUGHT SURVEY CERTIFICATE	0,10 m. waves		0,10 m. waves	
PGUA/DS/304/25	Wind force 01		Wind force 01	
	No tide flow		No tide flow	
	Weather: Fine		Weather: Cloudy	
DRAUGHT	INITIAL		FINAL	
Forward port	4,0400 m		13,2000 m	
Forward starboard	4,0900 m		13,1600 m	
Forward mean	4,0650 m		13,1800 m	
Stern correction	-0,1384 m		-0,0030 m	
Draught forward (corrected to fore perpendicular)	3,9266 m		13,1770 m	
Midship port	5,3500 m		13,3100 m	
Midship starboard	5,4200 m		13,2600 m	
Midship mean	5,3850 m		13,2850 m	
Midship correction	-0,0041 m		-0,0001 m	
Draught midship (corrected to midship perpendicular)	5,3809 m		13,2849 m	
Aft port	6,8200 m		13,2700 m	
Aft starboard	6,8400 m		13,2100 m	
Aft mean	6,8300 m		13,2400 m	
Stern correction	0,1348 m		0,0029 m	
Draught after (corrected to after perpendicular)	6,9648 m		13,2429 m	
Kell correction	0,0000 m		0,0000 m	
Waterplane coefficient correction for hull deflexion	0,0069 m		-0,0112 m	
Means of means corrected for deflexion:	5,4040 m		13,2549 m	
True trim	BY STERN	3,04 m	BY STERN	0,07 m
Heel (angle & in cm)	S 0.12 °	7,00 cm	P 0.09 °	5,00 cm
Hull deflexion:	HOGGING	6,48 cm	SAGGING	7,50 cm
DISPLACEMENTS	INITIAL		FINAL	
Displacement in salt water	32.954,7 t		86.072,9 t	
First trim correction	-732,3 t		4,8 t	
Second trim correction	45,4 t		0,0 t	
Displacement corrected for trim	32.267,7 t		86.077,7 t	
Water density	1,01850		1,01700	
Displacement corrected for density	32.063,1 t		85.405,9 t	
Deductibles (fresh water, oils, etc.)	19.511,2 t		1.853,1 t	
Displacement corrected for deductibles	12.551,9 t		83.552,8 t	
Light Ship	12.085,0 t			
Calculated constant	492,0 t			
Anchor + chain	25,1 t		0,0 t	
Total cargo loaded on board as per draught survey			70975,8 t	
Loading terminals: CB, CO, CT, RO, .	TPC	64,1 t/cm	TPC	70,4 t/cm
Cargo: Maize in bulk	MTC +0.5	936,4 t*cm	MTC +0.5	1214,4 t*cm
Paranaguá, Br - Brazil. October 18th, 2025	MTC -0.5	914,6 t*cm	MTC -0.5	1208,9 t*cm
Total cargo loaded on board as per shore scales			70.887,210 t	
Total cargo loaded on board as per draught survey			70.975,777 t	
Surplus	88,567 t		0,12 %	

Remarks: 1) Due to huge hull deflexion in sagging on final draft survey, it was applied the waterplane area coefficient correction for the deflexion formula as per UN/ECE/Energy/19/1992. 2) According to the Master/Chief Officer usual constant would amount to 480 t.

Standard Brazil Marine Surveys & Services Ltda

José Antonio Machado Gomes Pereira / Thiago Henrique Barbosa Verhagen

Licensed Marine Officer / Marine Surveyor / 375460MM

Master/Ch.Off: 70.968.800 t 81,590 t 0,12 %

Customs : 70.969.692 t 82,482 t 0,12 %

Owners: 70.952.697 t 65,487 t 0,09 %

Consignees: 70.959.568 t 72,358 t 0,10 %

Receivers: 70.962.921 t 75,711 t 0,11 %

10) INITIAL BALLAST CONDITION:

Date / Time : 15.10.25 /

08:40 h

Trim: 3,04 m

Vessel's	Observed	Pipe	Observed	Correction (m)		Corrected	Observed	Observed	Weight
Tank No.	Height (m)	A.D.L (m)	Sound. (m)	Trim	List	Sound. (m)	Volu. (m3)	Density	Total (t)
F.PK	24,36	0,32	0,07	-0,01	0,00	0,06	3,20	1,031	3,30
1 DB (P)	21,00	0,00	20,34	-0,16	0,00	20,18	1294,00	1,031	1334,10
1 DB (S)	20,92	0,00	20,38	-0,16	0,00	20,22	1303,40	1,031	1343,80
2 DB (P)	21,31	0,31	20,41	-0,18	0,00	20,23	1529,20	1,031	1576,60
2 DB (S)	21,34	0,33	20,12	-0,18	0,00	19,94	1463,40	1,031	1508,80
3 DB (P)	21,07	0,30	19,41	-0,33	0,00	19,08	2480,10	1,031	2557,00
3 DB (S)	20,98	0,30	18,64	-0,33	0,00	18,31	2236,20	1,031	2305,50
4 DB (P)	20,74	0,00	19,86	-0,49	0,00	19,37	2414,70	1,031	2489,60
4 DB (S)	20,75	0,00	20,25	-0,50	0,00	19,75	2498,60	1,031	2576,10
5 DB (P)	21,23	0,32	20,80	-0,11	0,00	20,69	1011,00	1,031	1042,30
5 DB (S)	21,23	0,32	20,29	-0,24	0,00	20,05	1003,70	1,031	1034,80
A.PK	12,91	0,32	0,19	0,01	0,00	0,20	1,00	1,031	1,00
TOTAL							17238,50		17772,90

11) FINAL BALLAST CONDITION:

Date / Time : 18.10.25 /

05:25 h

Trim: 0,07 m

Vessel's	Observed	Pipe	Observed	Correction (m)		Corrected	Observed	Observed	Weight
Tank No.	Height (m)	A.D.L (m)	Sound. (m)	Trim	List	Sound. (m)	Volu. (m3)	Density	Total (t)
F.PK	24,36	0,32	0,05	0,00	0,00	0,05	2,70	1,031	2,80
1 DB (P)	21,00	0,00	0,05	0,00	0,00	0,05	15,30	1,031	15,80
1 DB (S)	20,92	0,00	0,00	0,00	0,00	0,00	3,10	1,031	3,20
2 DB (P)	21,31	0,31	0,04	0,00	0,00	0,04	19,30	1,031	19,90
2 DB (S)	21,34	0,33	0,04	0,00	0,00	0,04	19,30	1,031	19,90
3 DB (P)	21,07	0,30	0,02	0,00	0,00	0,02	22,90	1,031	23,60
3 DB (S)	20,98	0,30	0,00	0,00	0,00	0,00	8,80	1,031	9,10
4 DB (P)	20,74	0,00	0,00	0,00	0,00	0,00	9,00	1,031	9,30
4 DB (S)	20,75	0,00	0,00	0,00	0,00	0,00	9,00	1,031	9,30
5 DB (P)	21,23	0,32	0,00	0,00	0,00	0,00	2,50	1,031	2,60
5 DB (S)	21,23	0,32	0,02	0,00	0,00	0,02	6,50	1,031	6,70
A.PK	12,91	0,32	0,18	0,00	0,00	0,18	0,90	1,031	0,90
TOTAL							119,30		123,10



12) INITIAL FRESH WATER CONDITION:

Vessel's	Observed	Pipe	Observed	Correction (m)		Corrected	Observed	Observed	Weight
Tank No.	Height (m)	A.D.L (m)	Sound. (m)	Trim	List	Sound. (m)	Volu. (m3)	Density	Total (t)
FWT (P)							107,00	1,000	107,00
FWT (S)							71,00	1,000	71,00
GWT (P)							0,00	1,000	0,00
TOTAL							178,00		178,00

13) FINAL FRESH WATER CONDITION:

Vessel's	Observed	Pipe	Observed	Correction (m)		Corrected	Observed	Observed	Weight
Tank No.	Height (m)	A.D.L (m)	Sound. (m)	Trim	List	Sound. (m)	Volu. (m3)	Density	Total (t)
FWT (P)							100,00	1,000	100,00
FWT (S)							55,00	1,000	55,00
GWT (P)							23,00	1,000	23,00
TOTAL							178,00		178,00

14) DEDUCTIBLES

	<u>INITIAL</u>	<u>FINAL</u>
INTERMEDIATE FUEL OIL	1410,1 t	1402,0 t
MARINE DIESEL OIL	150,2 t	150,0 t
LUBRICATING	K	K
FRESH WATER	178,0 t	178,0 t
BALLAST	17772,9 t	123,1 t
OTHERS	0,0 t	0,0 t
TOTAL	19511,2 t	1853,1 t



Digital documentation, photographs and vídeos:

MV LAAX

<https://standardbrazil.com.br/atendimentos/link?tag=PGUA/DS/304/25&tk=3502330183>



PARTICULARS

M.V. LAAX / BULK CARRIER

BUILDER: TSUNEISHI SHIP BUILDING CO. LTD
KEEL LAID: 29 October 2010
DELIVERED: 19 January 2012
HULL No: 1475
FLAG: MARSHALL ISLANDS
POR: MAJURO
I.M.O NO.: 9512355
CALL SIGN: V7XG9 OFF No.: 4478
SUEZ CANAL ID NO: 50086
PANAMA CANAL ID NO: 3012533

OWNER: BAILEY NAVIGATION COMPANY
ADDRESS: Trust Company Complex, Ajeltake road, Majuro, Marshall Islands MH96960
OPERATOR: GREHEL SHIPMANAGEMENT CO.
ADDRESS: 5-7 AGIOU SPYRIDONOS STREET, 185 53 PIRAEUS GREECE
PHONE: 30-2160705563
FAX:
E-Mail: info@grehel.com

COMMUNICATION	
INMARSAT C: 453850867 and 453850868	
Email 1: master@laax.grehel.com	
Email 2:	
VOICE 1: (FBB) +870773070006	
VOICE 2: BRIDGE (VSAT) +302112346526	
VOICE 3: MASTER (VSAT) +302112346524	
MMSI No: 538004478	

CLASS: NK
P and I: THE SWEDISH CLUB

DIMENSIONS	
LOA	228.99 m
LBP	222.00 m
BREADTH	32.26 m [MOULDED]
DEPTH	20.050 m [MOULDED]

LIGHT SHIP	12,085 MT	T.P.C.	70.57 MT
DISPLACEMENT	94,350.00	F.W.A.	333 mm

AIR DRAFTS	
KEEL TO TOP OF MAST:	49.9 m
KEEL TO HATCH COAMING TOP # 1:	22.60 m
KEEL TO HATCH COAMING TOP # 7:	22.60 m
DECK LINE TO HATCH COAMING TOP # 1:	2.55 m
DECK LINE TO HATCH COAMING TOP # 7:	2.55 m

SAFETY EQUIPMENT PROVIDED FOR:	25 PERSONS
--------------------------------	------------

HELICOPTER LANDING SITE	Hatch No.4
MAX HELICOPTER WEIGHT	4000 Kg

MAIN ENGINE	
TYPE	MITSUI MAN B&W 6S60MC-C
Max:	9710 kW AT 97.4 rpm.
Nominal:	8250 kW AT 92.3 rpm.
Shaft Power Limitation (ShaPoLi):	8363 kW

MOORING EQUIPMENT	
ANCHOR P&S	7425 Kg KHAC-14 HHP
CHAIN P&S	12 shackles, L - 330 m
LINES FWD	Polyprop 8 strand, 64mm dia, 200m
LINES AFT	Polyprop 8 strand, 64mm dia, 220m

CAPACITIES			
HOLD	CUM	CUFT	MAX WEIGHT
NO. 1	12,622.50	445,764.00	12,623
NO. 2	14,729.60	520,176.00	14,730
NO. 3	14,386.50	508,059.00	14,387
NO. 4	12,698.10	448,433.00	12,698
NO. 5	14,352.80	506,869.00	14,353
NO. 6	14,264.20	503,740.00	14,264
NO. 7	14,328.00	505,993.00	14,328
TOTALS:	97,381.70	3,439,034.00	

MAXIMUM CAPACITIES			
CARGO HOLDS		97,381.70	cum
BALLAST TANKS		22,060.90	cum
No. 4 HOLD		12,698.10	cum
F.W. TANK		468.8	cum

FREEBOARD, DRAFT & DEADWEIGHT				
	F'BOARD	DRAFT	TPC	DWT
SUMMER	5.676	14.429	70.57	82,265.00
FRESH W	5.343	14.762	70.59	82,257.00
TROPICAL	5.376	14.729	70.59	84,383.00
TROPICAL F	5.043	15.062	70.63	84,324.00
WINTER	5.976	14.129	70.54	80,148.00

TONNAGE			
	INT	SUEZ	PANAMA
GRT	43,013	44,389.77	43,013
NRT	27,239	41,533.65	27,239

PROPELLER	
TYPE	5 Blades Solid type, AEROFOIL SEC (KIS)
DIAMETER	6700 mm
IMMERSION	7.096m (fully immersed propeller)

DISTANCES	
27.75m	201.24m
Aft	Accommodation FWD end.
	Fwd



IMO CREW LIST

(Name of shipping line, agent, etc.)

Grebel Shipmanagement Co.

☒ Arrival ☐ Departure

Page No. 1/1

1. Name of ship: LAAX				2. Port of arrival/departure: PARANAGUA / BRAZIL				3. Date of arrival/departure: 15. 10. 25	
4. Nationality of ship: MARSHALL ISLANDS				5. Last port: FUJAIRAH / UAE				6. Nature and No. of identity document (passport, seaman book)	
7. No.	8. Family name, Given name (Passport)	9. Sex	10. Rank	11. Nationality	12. Date and place of birth	13. Country	14. Date and Place of Embarkation	15. Passport no. Exp. Date	16. Seaman bk no. Exp. Date
1	TYKHOLAZ OLEKSANDR	MALE	MASTER	UKRAINE	21-Jul-1982 UKRAINE	UKRAINE	19-Jun-2025 SAO FRANCISCO DO SUL / BRAZIL	FP599948 3-Jul-2028	AA 1004606 16-Oct-2029
2	SHCHERBANEV DENIS	MALE	CH.OFF	RUSSIAN FEDERATION	29-Mar-1979 USSR	RUSSIAN FEDERATION	31-Jul-2025 KHOR FAKKAN / UAE	77 3706526 10-Jun-2034	MK 0243771 NO
3	NADYEYEV STANISLAV	MALE	2ND OFF	UKRAINE	14-May-1986 UKRAINE	UKRAINE	11-Apr-2025 PORT SAID / EGYPT	FK640225 10-Jan-2028	AC007768 19-Jan-2028
4	DIACHENKO SERHII	MALE	2ND OFF	UKRAINE	31-Oct-1988 UKRAINE	UKRAINE	17-Mar-2025 DAMIETTA, EGYPT	F5761324 3-Oct-2028	AB672955 22-Jan-2026
5	BABIN SERGIY	MALE	CH.ENGR.	UKRAINE	4-Aug-1974 UKRAINE	UKRAINE	14-May-2025 KHOR FAKKAN / UAE	GA670267 9-Jul-2031	AB693715 29-Jun-2027
6	ABDOU AHMED MOHAMED AHMED ELKABBANY	MALE	2ND ENGR.	EGYPTIAN	26-Aug-1991 KAFRELSHIKH	EGYPT	14-May-2025 KHOR FAKKAN / UAE	A28071850 29-Mar-2028	S00049354 4-Dec-2029
7	JABIDI UMAR	MALE	3RD ENGR.	INDONESIA	4-Sep-1976 BOGOR	REPUBLIC OF INDONESIA	31-Jul-2025 KHOR FAKKAN / UAE	E4316930 21-Jul-2033	G 042833 10-Feb-2028
8	SAMEH SALAH ABDELRAZEK ALY MORSY	MALE	4TH ENGR.	EGYPTIAN	23-Jan-1984 MONOFIYA	EGYPT	31-Jul-2025 KHOR FAKKAN / UAE	A04459413 11-Dec-2031	S00036994 12-Nov-2028
9	KRASLYUK SERGIY	MALE	ELECTRICIAN	UKRAINE	10-Jun-1969 UKRAINE	UKRAINE	31-Jul-2025 KHOR FAKKAN / UAE	FH054161 24-Jul-2027	AC 004488 27-Dec-2027
10	MOHAMED BAGHAT ABDELHAKIM ISMAIL	MALE	BOSUN	EGYPTIAN	7-Mar-1967 BEHEIRA	EGYPT	5-Sep-2025 FUJAIRAH / UAE	A30167936 25-Mar-2029	S00021080 12-Feb-2027
11	AHMED MOHAMED FARAG GHARIB ABDELAAL	MALE	AB 1	EGYPTIAN	14-Dec-1998 ALEXANDRIA	EGYPT	19-Jun-2025 SAO FRANCISCO DO SUL / BRAZIL	A40971410 19-Mar-2032	S00052723 13-Apr-2030
12	TAUFIK	MALE	AB 2	INDONESIA	11-Nov-1990 SEPPONG	REPUBLIC OF INDONESIA	19-Jun-2025 SAO FRANCISCO DO SUL / BRAZIL	E1678219 30-Mar-2033	J 038482 13-May-2027
13	VINARSKIY NIKOLAY	MALE	AB 3	RUSSIAN FEDERATION	4-Jun-1988 USSR	RUSSIAN FEDERATION	31-Jul-2025 KHOR FAKKAN / UAE	66 6817936 22.03.2028	MK 0413162 NO
14	ANSAR HASAN	MALE	OS 1	INDONESIA	31-Aug-1992 SULI	REPUBLIC OF INDONESIA	19-Jun-2025 SAO FRANCISCO DO SUL / BRAZIL	X5895276 13-Jun-2035	G 035295 10-Dec-2027
15	ZEYAD ELSAYED ALY MOBARAK ABDELRAHMAN	MALE	DCDT	EGYPTIAN	5-Mar-2003 ALEXANDRIA	EGYPT	31-Jul-2025 KHOR FAKKAN / UAE	A27636035 9-Dec-2027	S00043229 23-Jun-2029
16	RENALDI	MALE	OILER 1	INDONESIA	20-Nov-1994 BOTTA	REPUBLIC OF INDONESIA	17-Jan-2025 ITAQUI, BRAZIL	E0789061 21-Oct-2032	H 021358 23-May-2027
17	MAHMOUD SAAD KASSEM KASSEM	MALE	OILER 2	EGYPTIAN	1-Oct-1996 BEHEIRA	EGYPT	16-Mar-2025 DAMIETTA, EGYPT	A26106996 17-Nov-2026	S00042148 14-May-2029
18	IRHAS ASMAD	MALE	OILER 3	INDONESIA	16-Oct-1990 TUMBU BARA	REPUBLIC OF INDONESIA	14-May-2025 KHOR FAKKAN / UAE	C8907879 8-Apr-2027	H 018307 21-Mar-2027
19	YESKE YEVGENIY	MALE	FITTER	UKRAINE	26-Aug-1982 UKRAINE	UKRAINE	19-Jun-2025 SAO FRANCISCO DO SUL / BRAZIL	FM617592 4-Apr-2028	AB626730 12-Apr-2028
20	MOHAMED MANSOUR IBRAHIM ABDELRAZEK RADY	MALE	ECDT	EGYPTIAN	28-Mar-2003 ALEXANDRIA	EGYPT	11-Apr-2025 PORT SAID / EGYPT	A36623123 9-Feb-2031	S00037010 25-Nov-2028
21	AMIR ABDELNABY SHEHATA MOHAMED MAHMOUD	MALE	COOK	EGYPTIAN	26-Nov-1981 ALEXANDRIA	Egypt	30-Jul-2025 KHOR FAKKAN / UAE	A37061414 8-Mar-2031	S00053614 10-May-2030
22	EDI	MALE	AST.COOK	INDONESIA	11-Oct-1993 PURBALINGGA	REPUBLIC OF INDONESIA	14-May-2025 KHOR FAKKAN / UAE	X5013392 23-Apr-2035	F 051236 23-Apr-2026
23	YUSRIL PARURA	MALE	MSM	INDONESIA	4-Jun-2001 JAKARTA	REPUBLIC OF INDONESIA	17-Jan-2025 ITAQUI, BRAZIL	E1629586 20-Dec-2032	H 096208 15-Dec-2025

18. Signature by master

MASTER OF MV "LAAX"

CAPT. TYKHOLAZ OLEKSANDR




m.v. "Laax"

PRE - STOWAGE PLAN

DATE	25.10.25
VOYAGE NO.	04/2025
LOADING PORT	Paranagua, Brazil
DISCHARGING PORT	Iran
CARGO	Corn in bulk
STOWAGE FACTOR	45.5 cuft/mt
DOCK DENSITY	1.016

DWT Breakdown		
HFO		1,454.0 mt
MDO		150.4 mt
Ballast	APT	0.0 mt
	unpumpable	200.0 mt
Fresh Water		150.0 mt
D.W. Constant		500.0 mt
Cargo		71,065.000 mt
Total		73,519.4 mt

Total Cargo 71,065.000 mt

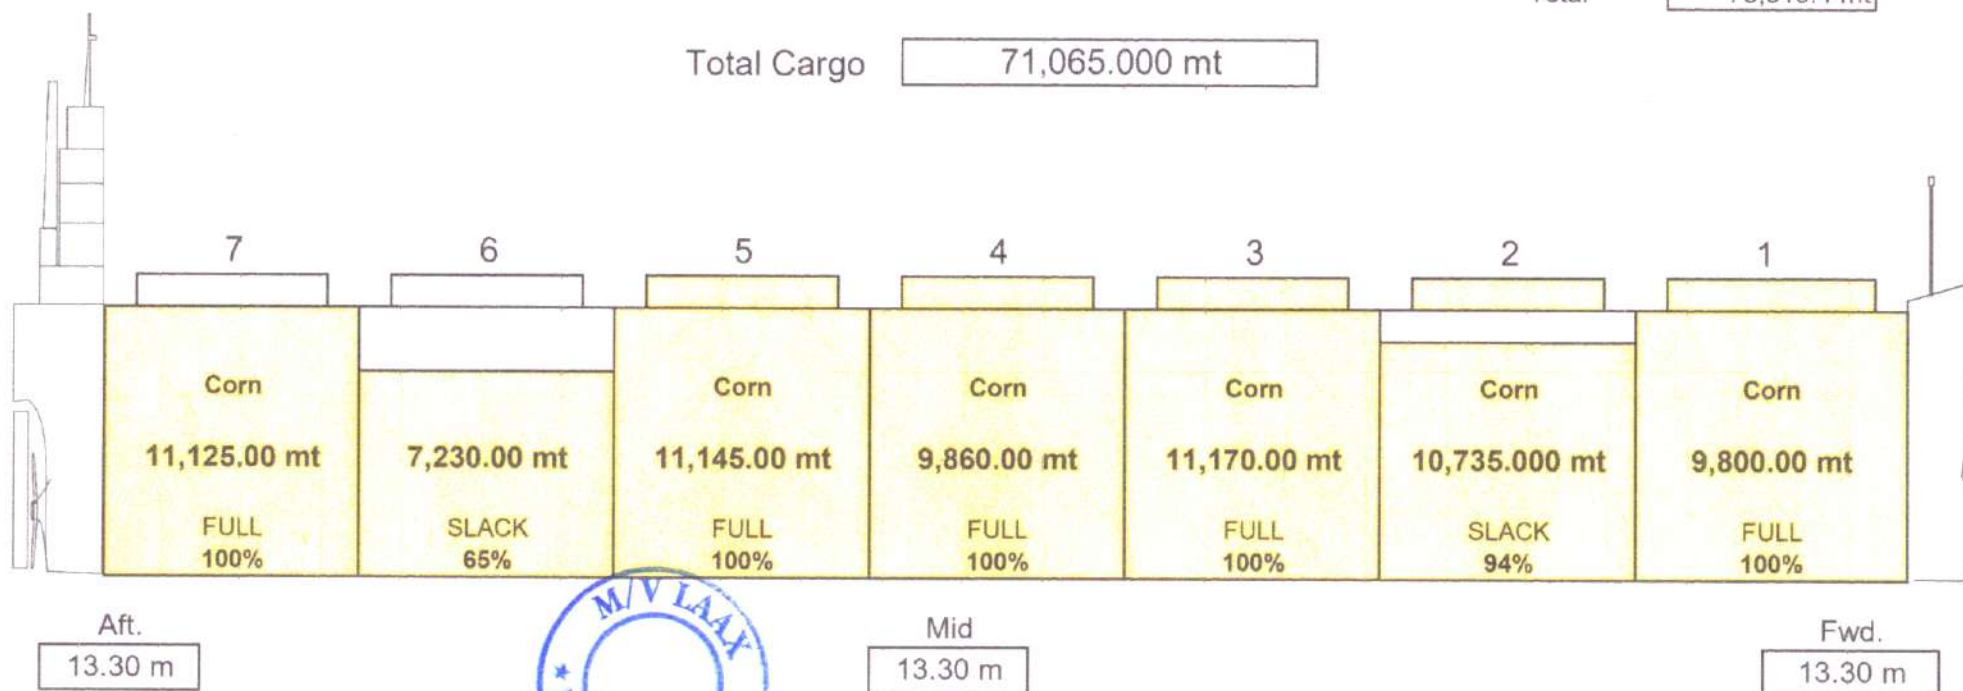

Master  Oleksandr Tykholaz

Ch. Off.  Denis Shcherbaney

The provided Pre-Loading Stowage Plan is an estimate based on the charterer's agents supplied information and best information available to the company and will always be subject to change and re-assessment made at any stage upon information as it becomes available or becomes significant and to overriding issues in relation to safety.

Loading Plan

LOADING PLAN		Version 2	VESSEL: m/v "Laax"				VOY NO. 04/25								
Loading Port:		Cargo(es): CORN IN BULK	Assumed stowage Factor of cargo(es): abt 45.5' CF/MT		Ballast pump rate: 1x1500 m3 / 1hr	Dock water density: 1.016	Max draught available(W): 13.3 m	Max air draught In berth: 18.0 M							
Paranagua / BRAZIL															
Discharging Port :		Last cargo: CORN IN BULK	No. of unloaders: 2		Loading rate: abt. 1400 MT / h each one		Min draught available(W): N/A	Max Departure draught: 13.3 m							
IRAN															
		7	6	5	4	3	2	1							
Tons:		SF 45.5' cft/mt	SF 45.5' cft/mt	SF 45.5' cft/mt	SF 45.5' cft/mt	SF 45.5' cft/mt	SF 45.5' cft/mt	SF 45.5' cft/mt							
		11125.000 MT	7230.00 MT	11145.000 MT	9860.000 MT	11170.000 MT	10735.000 MT	9800.000 MT							
Grade:		CORN	CORN	CORN	CORN	CORN	CORN	CORN							
		100.00%	65.00%	100.00%	100.00%	100.00%	94.00%	100.00%							
Total CGO : 71065.000 MT															
Oper No.	Cargo		BALLASTING OPERATIONS	Time required (hours)	Comments	Calculated values				Calculated values			Observed Values		
	Hold No.	Tons				Draught		Maximum		Air draught	Draught mid	Trim	Draft		
						FWD	AFT	SF	BM				FWD	AFT	MID
						4.30	7.20	46%	48%	42.90	5.75	2.90			
1A	3	8000								17.30					
1B	5	8000	PO WBT #2 P&S; PO WBT #4	5.7h / 5.7h		5.40	8.14	61%	50%	16.70	6.87	2.53			
2A	1	4500								16.70					
2B	4	4500	PO WBT #1 P&S; WBT#3 P&S / 30%	3.2h / 3.2h		6.88	8.12	68%	50%	15.90	7.50	1.24			
3A	2	8000								15.50					
3B	7	8000	PO WBT #3 P&S 70%; Stripping WBT # 1-4	5.7h / 2.8h	Stripping WBT # 1-4	7.67	10.87	47%	41%	14.70	9.27	3.19			
4A	4	5360			Complete CH #4					13.40					
4B	6	6230	PO WBT #5 P&S; Stripping WBT # 1-5	3.8h/1.4h	Remains 1000mts FO Trimming	8.73	12.51	51%	46%	12.70	10.62	3.78			
5A	1	5300			Complete CH #1					13.40					
5B	7	3125	Stripping WBT # 1-5	2.3h/ 2.3h	Complete CH #7	11.02	12.66	59%	36%	10.80	11.84	1.64			
6A	3	3170			Complete CH #3					11.00					
6B	5	3145	Stripping WBT # 1-5	2.5h /	Complete CH #5	12.20	13.29	68%	48%	10.70	12.74	1.08			
7	2	1735		1.2h	Remains 1000mts FO Trimming	12.93	13.08	84%	74%	10.20	13.00	0.15			
TRIMMING CH 2 & 6															
8A	2	1000			Complete CH #2					9.70					
8B	6	1000			Complete CH #6	13.30	13.30	86%	79%	9.60	13.30	0.00			
TOTAL DE - BALLASTING TIME 13 HRS															
KEEP SHIP UPRIGHT ALL TIME															
DEPARTURE (Seagoing condition. (denc.=1.025))															
Total CGO : 71065.000						13.16	13.22	86%	-79%	36.70	13.19	0.05			
NO DEVIATION FROM ABOVE PLAN WITHOUT APPROVAL OF CHIEF MATE OPERATION TO BE NUMBERED 1A, 1B, 2A, 2B, ETC. WHEN USING TWO LOADERS ABBREVIATIONS: PI=PURAP IN GI=GRAVITATE IN F=FULL PO=PURAP OUL GO=GRAVITATE OUT MT=EMPTY ALL ENTRIES WITHIN THE LIST MUST BE COMPLETED AS FAR AS POSSIBLE. THE ENTRIES OUTSIDE THE BOX ARE OPTIONAL.				SIGNED CH OFF		SIGNED OOW		BENDING MOMENTS (BM) & SHEAR FORCES (SF) ARE TO BE EMPRESSED AS A %AGE OF MAXIMUM PERMITTED IN-PORT VALUES FOR INTERMEDIATE STAGES AND OF MAXIMUM PERMITTED AT-SEA VALUES FOR THE FINAL STAGE. EVERY STEP IN THE LOADING/UNLOADING PLAN MUST REMAIN WITHIN THE ALLOWABLE LIMITS FOR HULL GIRDER SHEAR FORCES. BENDING MOMENTS AND TONNAGE PER HOLD, WHERE APPLICABLE. LOADING/UNLOADING OPERATIONS MAY HAVE TO BE PASSED TO ALLOW FOR BALLASTING/DEBALLASTING IN ORDER TO KEEP ACTUAL VALUES WITHIN LIMITS.							
				SIGNED TERMINAL		SIGNED OOW									
 MASTER 															

MV "LAAX"	INITIAL SURVEY		FINAL SURVEY	
	Inner roads 9.1		Wharf 213	
	15.10.2025 - 08:10 h		18.10.2025 - 04:50 h	
	0,10 m. waves		0,10 m. waves	
IMO NO. 9512355	FLAG: Marshall Islands		BUILD: 2012	
DRAUGHT SURVEY CERTIFICATE	No tide flow		No tide flow	
PGUA/DS/304/25	Weather: Fine		Weather: Cloudy	
DRAUGHT	INITIAL		FINAL	
Forward port	4,0400 m		13,2000 m	
Forward starboard	4,0900 m		13,1600 m	
Forward mean	4,0650 m		13,1800 m	
Stem correction	-0,1384 m		-0,0030 m	
Draught forward (corrected to fore perpendicular)	3,9266 m		13,1770 m	
Midship port	5,3500 m		13,3100 m	
Midship starboard	5,4200 m		13,2600 m	
Midship mean	5,3850 m		13,2850 m	
Midship correction	-0,0041 m		-0,0001 m	
Draught midship (corrected to midship perpendicular)	5,3809 m		13,2849 m	
Aft port	6,8200 m		13,2700 m	
Aft starboard	6,8400 m		13,2100 m	
Aft mean	6,8300 m		13,2400 m	
Stem correction	0,1348 m		0,0029 m	
Draught after (corrected to after perpendicular)	6,9648 m		13,2429 m	
Kell correction	0,0000 m		0,0000 m	
Waterplane coefficient correction for hull deflexion	0,0069 m		-0,0112 m	
Means of means corrected for deflexion:	5,4040 m		13,2549 m	
True trim	BY STERN	3,04 m	BY STERN	0,07 m
Heel (angle & in cm)	S 000 °	7,00 cm	P 000 °	5,00 cm
Hull deflexion:	HOGGING	6,48 cm	SAGGING	7,50 cm
DISPLACEMENTS	INITIAL		FINAL	
Displacement in salt water	32.954,7 t		86.072,9 t	
First trim correction	-732,3 t		4,8 t	
Second trim correction	45,4 t		0,0 t	
Displacement corrected for trim	32.267,7 t		86.077,7 t	
Water density	1,01850		1,01700	
Displacement corrected for density	32.063,1 t		85.405,9 t	
Deductibles (fresh water, oils, etc.)	19.511,2 t		1.853,1 t	
Displacement corrected for deductibles	12.551,9 t		83.552,8 t	
Light Ship	12.085,0 t			
Calculated constant	492,0 t			
Anchor + chain	25,1 t		0,0 t	
Total cargo loaded on board as per draught survey			70975,8 t	
Loading terminals: CB, CO, CT, RO, .	TPC	64,1 t/cm	TPC	70,4 t/cm
Cargo: Maize in bulk	MTC +0.5	936,4 t/cm	MTC +0.5	1214,4 t/cm
Paranaguá, Br - Brazil. October 18th, 2025	MTC -0.5	914,6 t/cm	MTC -0.5	1208,9 t/cm
Total cargo loaded on board as per shore scales			70.887,210 t	
Total cargo loaded on board as per draught survey			70.975,777 t	
Surplus	88,567 t		0,12 %	

Remarks: 1) Due to huge hull deflexion in sagging on final draft survey, it was applied the waterplane area coefficient correction for the deflexion formula as per: UN/ECE/Energy/18/1992. 2) According to the Master/Chief Officer usual constant would amount to 480 t.

Standard Brazil Marine Surveys & Services Ltda.

José Antonio Machado Gomes Pereira / Thiago Henrique Barbosa Verhagen

Licensed Marine Officer / Marine Surveyor / 375460MM

Master/Ch.Off:	70.968,800 t	81,590 t	0,12 %
Customs :	70.969,692 t	82,482 t	0,12 %
Owners:	70.952,697 t	85,487 t	0,09 %
Consignees:	70.959,568 t	72,358 t	0,10 %
Receivers:	70.962,921 t	75,711 t	0,11 %

Master/Ch.Off:



CARGONAVE

STOWAGE PLAN

M/V " LAAX "

MARSHALL ISLANDS - FLAG

PORT OF : PARANAGUÁ, BRAZIL

DATE : OCTOBER 18TH, 2.025.

	7	6	5	4	3	2	1
	10.805.640 MT	7.903.120 MT	11.084.795 MT	9.749.040 MT	11.054.775 MT	10.848.900 MT	9.440.940 MT
	FEED CORN-GMO, PACKING	FEED CORN-GMO, PACKING	FEED CORN-GMO, PACKING	FEED CORN-GMO, PACKING	FEED CORN-GMO, PACKING	FEED CORN-GMO, PACKING	FEED CORN-GMO, PACKING
	IN BULK	IN BULK	IN BULK	IN BULK	IN BULK	IN BULK	IN BULK
	FULL	SLACK	FULL	FULL	FULL	SLACK	FULL
CUBIC FEET	505.993	503.740	506.869	448.433	508.059	520.176	445.764
ST. FACTOR	46,83		45,73	46,00	45,96	47,95	47,22

TOTAL CARGO LOADED: 70.887 MT OF FEED CORN-GMO, PACKING IN BULK /// AVERAGE S/F 46,34 CBT / MT



AGENCIA MARITIMA CARGONAVE LTDA.

Avenida Gabriel de Lara, 1.040

Paranagua - PR - Brazil

83.203-550

E-Mail : cargonave@cargonave.com.br

NAVIO:	LAAX
AGÊNCIA:	AGÊNCIA MARITIMA CARGONAVE LTDA
OPERADOR:	AGÊNCIA MARITIMA CARGONAVE LTDA
DATA EMBARQUE:	18.10.2025
PESO TERRA:	70.887,210
PESO BORDO:	70.975,777
VARIAÇÃO:	88,567
PERCENTUAL:	0,12%
Entrar na estatística	Sim

PORÃO	1	2	3	4	5	6	7	TOTAL
PRODUTO	MAIZE	MAIZE	MAIZE	MAIZE	MAIZE	MAIZE	MAIZE	
AGTL								0,000
CARGILL								0,000
CENTRO SUL								0,000
CIMBESSUL	5.408,285	3.345,185	3.053,585	5.246,990	503,370	286,750		17.844,165
COAMO	1.463,920	6.335,230	8.001,190	4.502,050	2.575,600	7.616,370	10.805,640	41.300,000
CORREDOR - V								0,000
CORREDOR - H								0,000
COTRIGUAÇU	994,175				8.005,825			9.000,000
INTERALLI								0,000
DREYFUS								0,000
ROCHA	1.574,560	1.168,485						2.743,045
TOTAL	9.440,940	10.848,900	11.054,775	9.749,040	11.084,795	7.903,120	10.805,640	70.887,210
CUBAGEM	445.764	520.176	508.059	448.443	506.869	503.740	505.993	
FATOR DE ESTIVA	47,22	47,95	45,96	46,00	45,73	63,74	46,83	
CONDIÇÃO PORÃO	FULL	SLACK	FULL	FULL	FULL	SLACK	FULL	

Observações:
